


Agile Project Management

Task Board

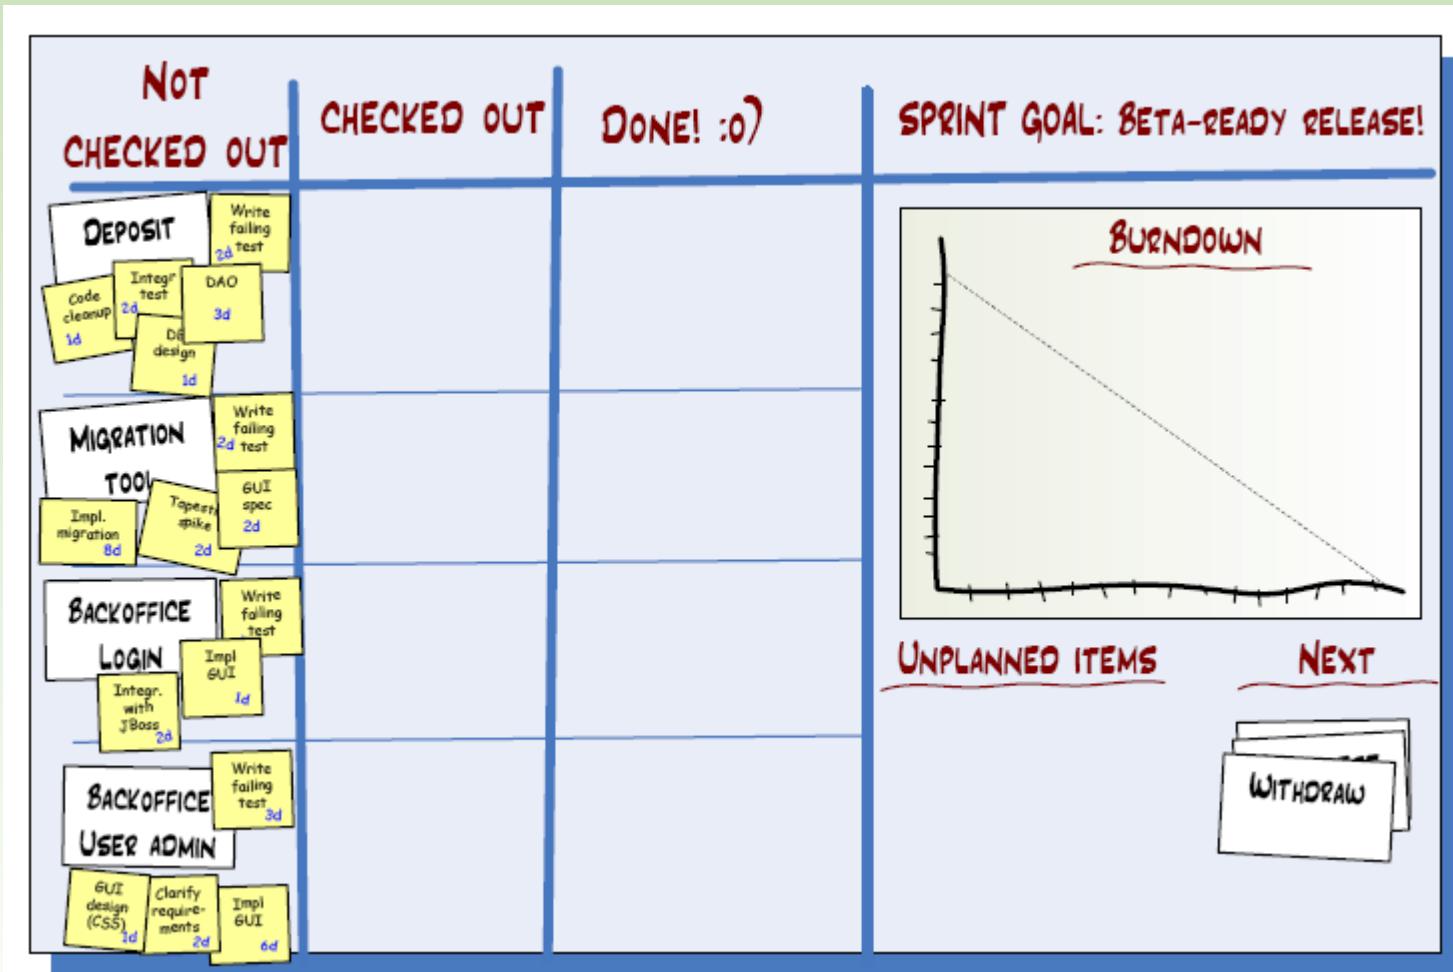


Agile Project Management

Task Board Layout


Sprint Board Layout					
Project Code & Name	<proj code - proj name>	Scrum Master: <name/initial>	Sprint Number: #	Sprint Start Date: <dd/mm/yyyy>	Sprint Demo Date: <dd/mm/yyyy>
Story ID & Story Des	Planned	In Progress	To Be Verified	Done	Burn Down Chart
<story ID> <write story name / description here>	<paste sticky notes for various tasks to implement the user story - those tasks in 'Planned' status>	<paste sticky notes for various tasks to implement the user story - those tasks in 'In Progress' status>	<paste sticky notes for various tasks to implement the user story - those tasks in 'To Be Verified' status>	<paste sticky notes for various tasks to implement the user story - those tasks in 'Done' status>	<plot burn down chart in this area>
					Unplanned Tasks <paste sticky notes for tasks identified after sprint planning>
					Next Sprint Tasks <paste sticky notes for tasks in the next sprint>

Agile Project Management

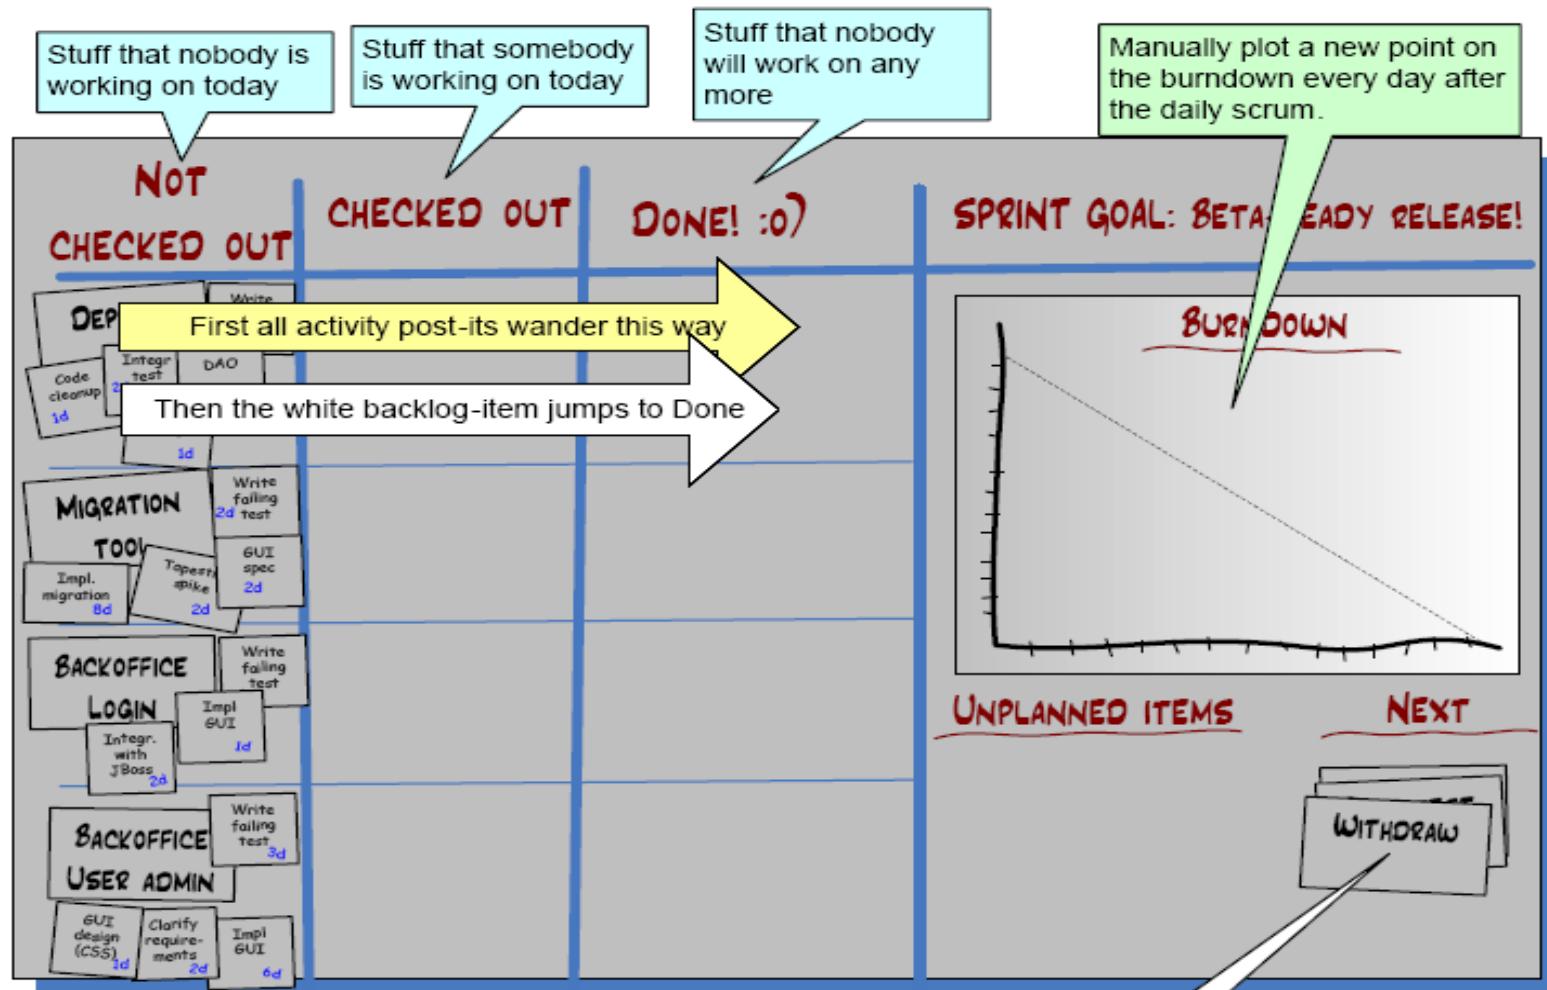


If all backlog items
are completed
before the sprint
ends, add new
ones from here.

Agile Project Management

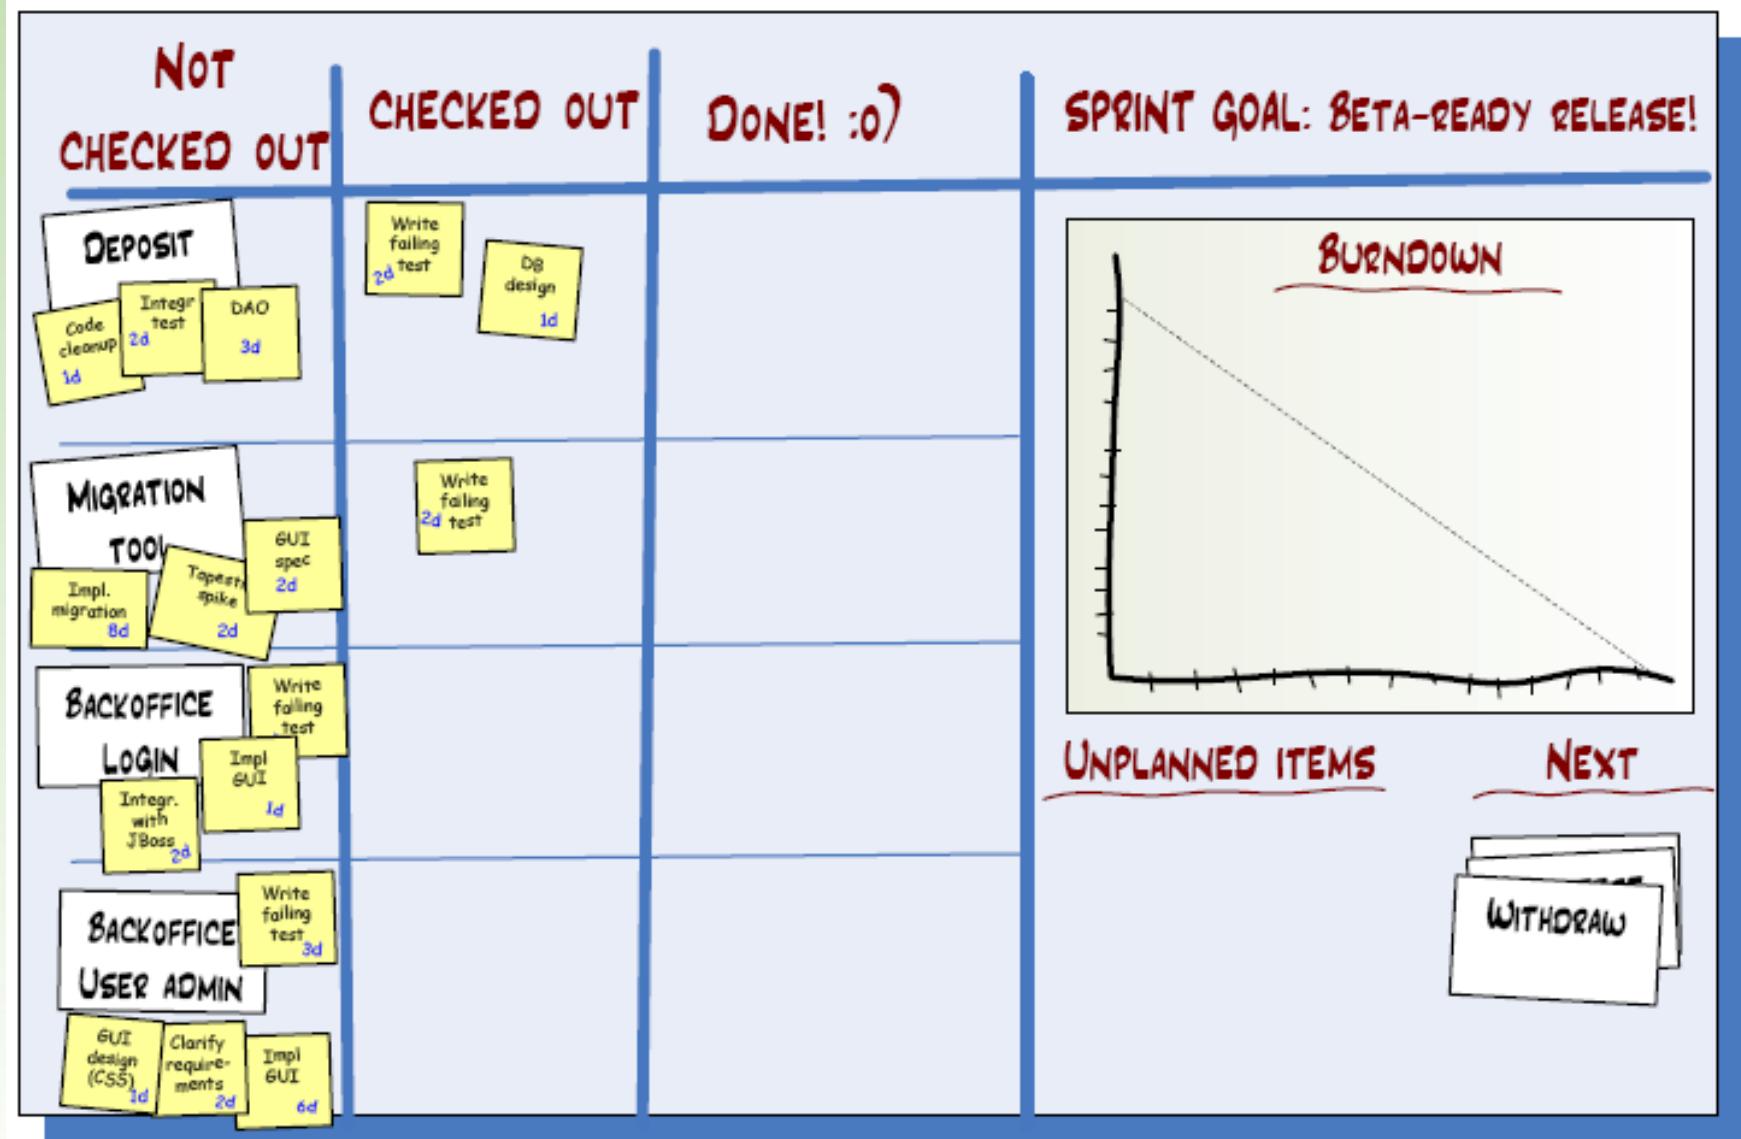

Agile Project Management

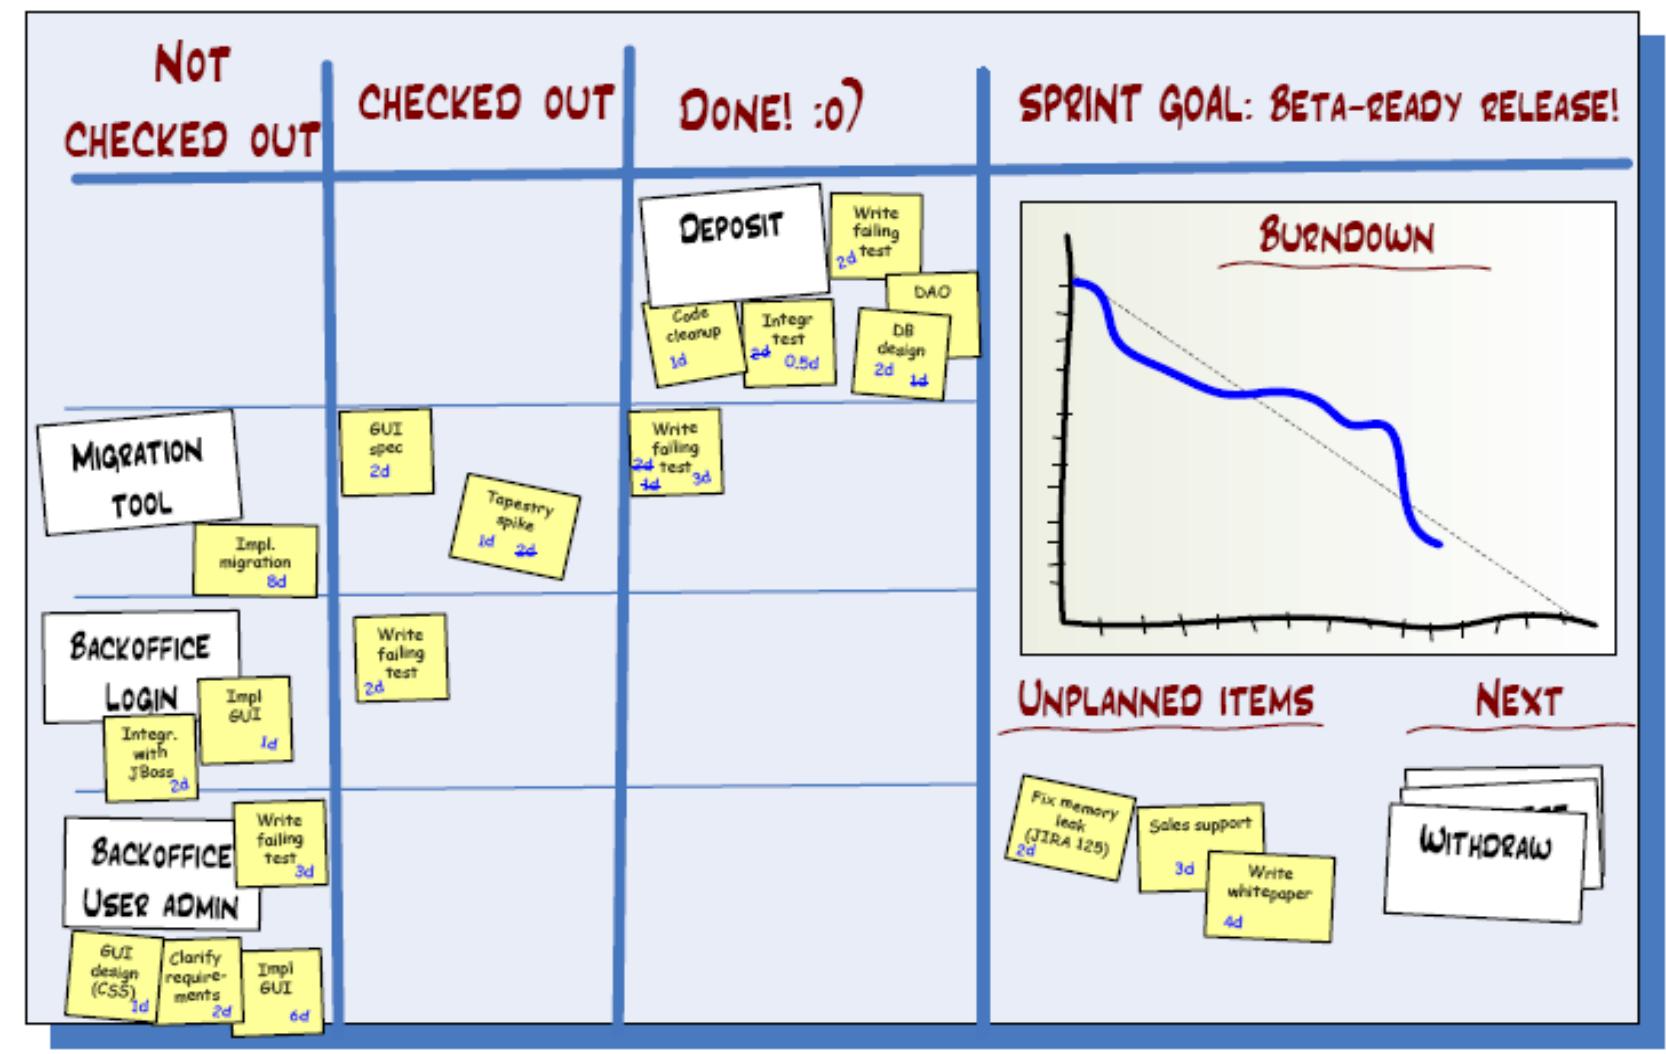

Agile Project Management

Sprint Backlog

	A	B	C	D	E	F	G	H	I	J	K	L	M	N	O	P
1	Sprint 1 Backlog															
2																
3																
4																
5																
6																
7	Sort Sprint Tasks				Update Task Slips											
8																
9	Sprint implementation days				8	Effort Remaining on implementation day...										
10	Trend calculated based on last				8	Days	Totals	211	211	189	175	167	147	107	62	23
11						Story ID	Responsible	Est.	1	2	3	4	5	6	7	8
12	Task name					Status										
13																
14																
15	Design Meeting				1	All	Done	10	10	0	0	0	0	0	0	0
16	SRS Update				1	BI	Done	3	3	0	0	0	0	0	0	0
17	Database Design Update				1	MG	Done	3	3	0	0	0	0	0	0	0
18	DB script preparation & DB tables creation				1	MG	Done	4	4	4	1	0	0	0	0	0
19	Test data and master data creation (write script & create)				1	BI	Done	4	4	4	2	0.5	0	0	0	0
20	Screen Design Update				1	NB, S	Done	8	8	4	3	1.5	1.5	1.5	1.5	0
21	Class Design Documentation				1	NPR	Ongoing	4	4	2	2	1	1	1	1	1
22	General configuration / parameter creation				1	NPR	Done	2	2	2	2	0	0	0	0	0
23	Template Design				1	NPR	Done	8	8	8	0	0	0	0	0	0
24	Coding - Zend Implementation of Form Validation				1	NB, BI	Done	30	30	30	30	30	30	20	10	0
25	Coding - Form Style Sheet Implementation				1	NPR, MG, SK	Done	30	30	30	30	30	30	20	5	0
26	Coding - Form Data Insertion				1	NPR, BI, MG	Ongoing	30	30	30	30	30	30	30	10	3
27	Unit Testing				1	All	Ongoing	20	20	20	20	20	20	20	20	10
28	Code Review				1	NPR, NB	Ongoing	10	10	10	10	10	10	10	10	5
29	Integration				1	NPR	Planned	4	4	4	4	4	4	4	4	4
30	Unplanned Tasks															
31	VSS Training					KSM	Done	1	1	1	1	0	0	0	0	0
32	Coding - Zend Framework Familiarisation					ALL	Done	40	40	40	40	40	20	0	0	0
33																

